

Work Order

Mooring Operations, Engineering and Field Support

Work Order No.		15122		Work Order Prepared by:	
Job Name:		Atlantis Forestay		Molyneaux	
Date Received:		5/27/2015			
Project No:		51074			
Requested by:		Patrick Hennessy			
Organization:		Atlantis			
Due Date:	Checked for shipment	5/28/2015	5/28/15	Completed	Initials CM
Ship Date:				Picked Up	
Fabricate or prepare	In Storage	Qty to ship	Item	Factory Reel No.	Chgd/Ordered
			Wire Fabrication		
CM 1 ✓		1	✓ nm 4.8m shot of 3/8" Nilspin Wire, Shot No. 15122-1 Correction: 4.7948M (Same as sample provided)	428-474994-1	
Supplies to be Charged out or Purchased					
Staging/Shipping: List items being shipped (not contents)					
		<u>Qty</u>	<u>Description</u>	<u>Delivery Location</u>	<u>Date</u>



WOODS HOLE OCEANOGRAPHIC INSTITUTION

MOORING LAB


WOODS HOLE, MA 02543

508-289-2395

CERTIFICATE OF TEST

TEST INFORMATION

PROJECT	Atlantis Forestay
TEST #	00241
TEST DATE	5/28/2015
TEST TYPE	3/8 NIL
SAMPLE #	15122-1
TEST DESCRIPTION	
Reel # 428-474994-1 Project # 51074	

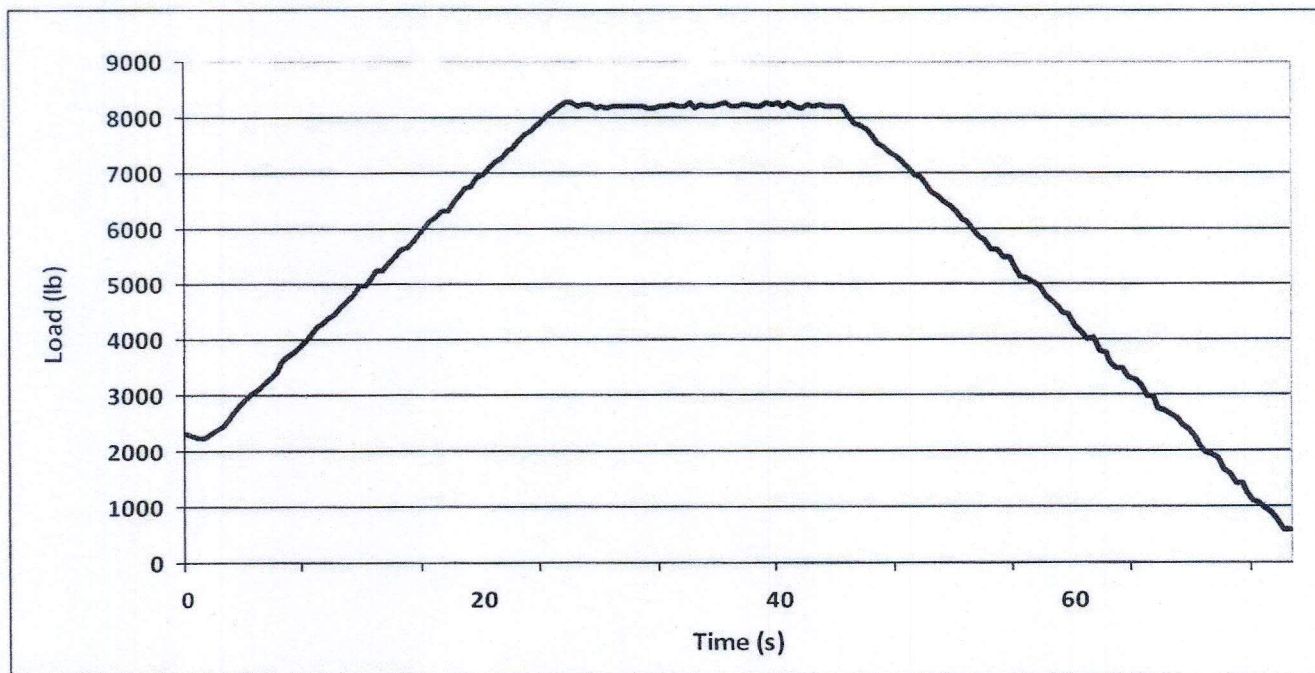

TEST RESULTS

MAX LOAD 8350 lb

OPERATOR Meissner




WOODS HOLE OCEANOGRAPHIC INSTITUTION
MOORING LAB
WOODS HOLE, MA 02543
508-289-2395

CERTIFICATE OF TEST

TEST INFORMATION

PROJECT	Atlantis Forestay
TEST #	00242
TEST DATE	5/28/2015
TEST TYPE	3/8 NIL
SAMPLE #	15122-1
TEST DESCRIPTION	Reel # 428-474994-1 Project # 51074

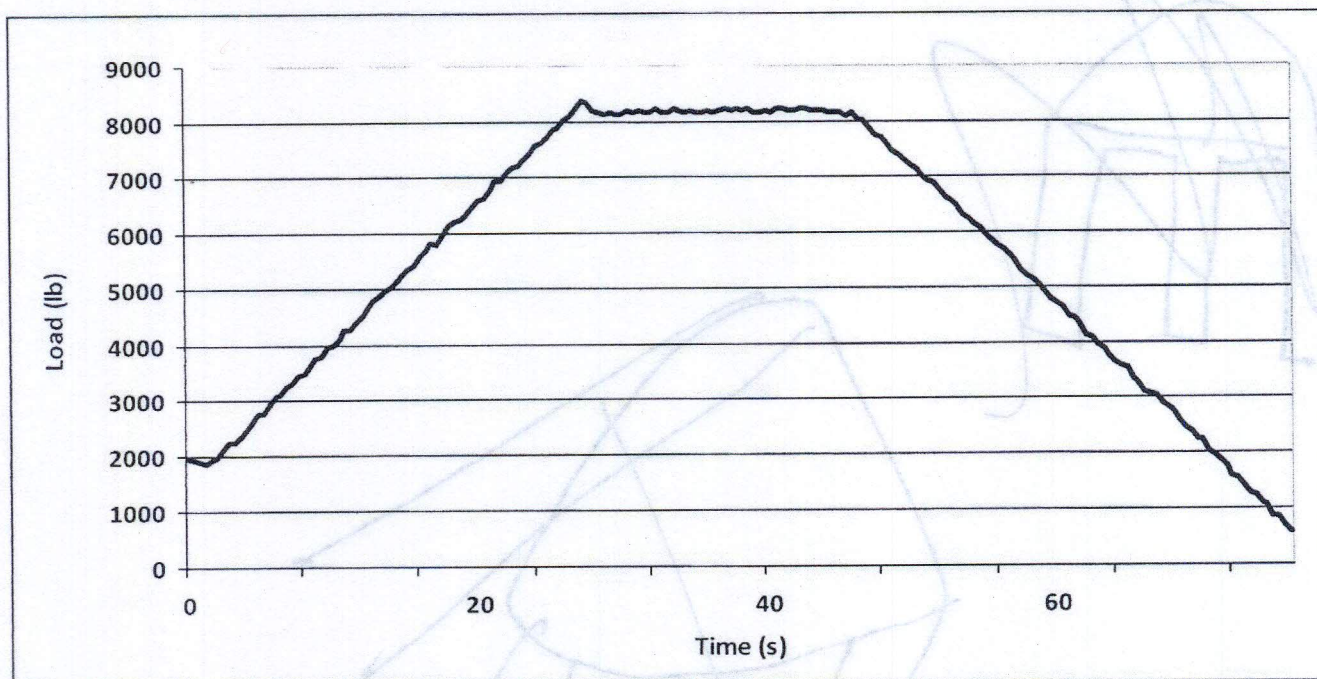

TEST RESULTS

MAX LOAD 8375 lb

OPERATOR Meissner
